Activity ID	Activity Name	Original Duration	Remaining Duration	Total Float	Activity % Complete	Start	Finish
MIC-EH Connector Schedule - 3_2008 Update		2985	980	0		01-Jun-00 A	17-Dec-11
PLANNING		1527	0	980		01-Jun-00 A	04-Apr-06 A
PLAN		1527	0	980		01-Jun-00 A	04-Apr-06 A
PL010	PROJECT NTP	0	0		100%	01-Jun-00 A	
PL020	FDOT FUNDS RELEASED	0	0		100%	03-Jul-00 A	03-Jul-00 A
PL030	PREPARE/FINALIZE JPA WITH FDOT	30	0		100%	05-Jul-00 A	03-Aug-00 A
PL040	JPA APPROVED BY BCC	60	0		100%	04-Aug-00 A	19-Sep-00 A
PL050	ISSUE W.O. TO PARSONS UNDER EXIST. FDOT CONTRACT	7	0		100%	23-Jan-01 A	29-Jan-01 A
PL060	PERFORM DRAFT EIS (DEIS)	757	0		100%	30-Jan-01 A	25-Sep-03 A
PL070	PREP. FTA P.E. REQUEST/NEW STARTS DOC. PACKAGE	171	0		100%	15-Dec-03 A	20-Aug-04 A
PL080	PREPARE PROJECT MANAGEMENT PLAN	60	0		100%	15-Mar-04 A	30-Jul-04 A
PL090	PB FINALIZES RIDERSHIP NUMBERS-EARLINGTON HGHTS.	30	0		100%	06-May-04 A	19-Aug-04 A
PL100	P.E. REQUEST PACKAGE TO FTA	0	0		100%	20-Aug-04 A	20-Aug-04 A
DE005	DECISION TO PROCEED 100% LOCAL FUNDS	7	0		100%	12-Oct-04 A	12-Oct-04 A
DE010	NEW LPA ALIGNMENT (2.4 MILES) PRESENTED TO MPO	78	0		100%	04-Feb-05 A	23-Jun-05 A
DE015	PROCESS JPA WITH FDOT THROUGH BCC & CITT	147	0		100%	03-May-05 A	25-May-05 A
DE016	REVISED LPA ALIGNMENT TO MPO AS INFORMATION ITEM	0	0		100%		23-Jun-05 A
DE017	MPO APPROVAL OF REVISED ALIGNMENT (2.4 MILES)	181	0		100%	24-Jun-05 A	23-Mar-06 A
DE020	PREP ENVIRONMENTAL ASSESSMENT(EA)-US COAST GUARD	143	0		100%	15-Aug-05 A	30-Jan-06 A
DE112	EA APPROVALS & CIRCULATION PERIOD (USCG)	97	0		100%	31-Jan-06 A	04-Apr-06 A
DE132	FONSI ISSUED BY USCG	0	0		100%		04-Apr-06 A
PUBLIC INVOLVEMENT		1304	714	168		29-Nov-05 A	09-Dec-10
PLAN		1304	714	168		29-Nov-05 A	09-Dec-10
DE150	Public Involvement During Design	695	0	278	100%	29-Nov-05 A	15-Mar-08
DE270	Public Involvement During Construction	516	516	168	0%	18-Dec-08	09-Dec-10
AGENCY DELIVERABLES		1177	610	167		01-Jan-06 A	17-Jul-10
DESIGN-MDT DELIVERABLES-Pt 1 Technical Criteria		431	0	5		01-Jan-06 A	07-Nov-07 A
MDT255	MDT finalize design criteria	614	0		100%	01-Jan-06 A	09-Sep-07 A
MDT250	MDT proc. docs-3rd Rail suprts/coverbrd	83	0		100%	12-Jun-07 A	07-Nov-07 A
FARE COLLECTION EQUIPMENT (FCE)		720	610	167		26-Sep-07 A	17-Jul-10
MDT200	MDT Procurement Process - Fare Collection Vendor	97	76	235	21.65%	26-Sep-07 A	29-May-08
MDT205	NTP to Fare Collection Vendor	0	0	235	0%		29-May-08
MDT240	Coordination of Fare Collection Design & Construction	778	778	235	0%	30-May-08	16-Jul-10
MDT210	FCE Delivery for MIC/EHT Station	0	0	235	0%		16-Jul-10
MDT215	Begin FCE Installation	0	0	235	0%	17-Jul-10	
DESIGN		757	10	970		17-Apr-05 A	29-Mar-08
15 % DESIGN		108	0	0		17-Apr-05 A	19-Sep-05 A
DE090	15% Design Phase	155	0		100%	17-Apr-05 A	19-Sep-05 A
DE095	15% DESIGN CONTROL POINT	0	0		100%		19-Sep-05 A
30 % DESIGN		98	0	0		20-Dec-05 A	15-May-06 A
DE100	30% Design Phase -Civil, Track Work, Systems	100	0		100%	20-Dec-05 A	13-Mar-06 A
DE110	30% Design Phase -Station Design	137	0		100%	20-Dec-05 A	05-May-06 A

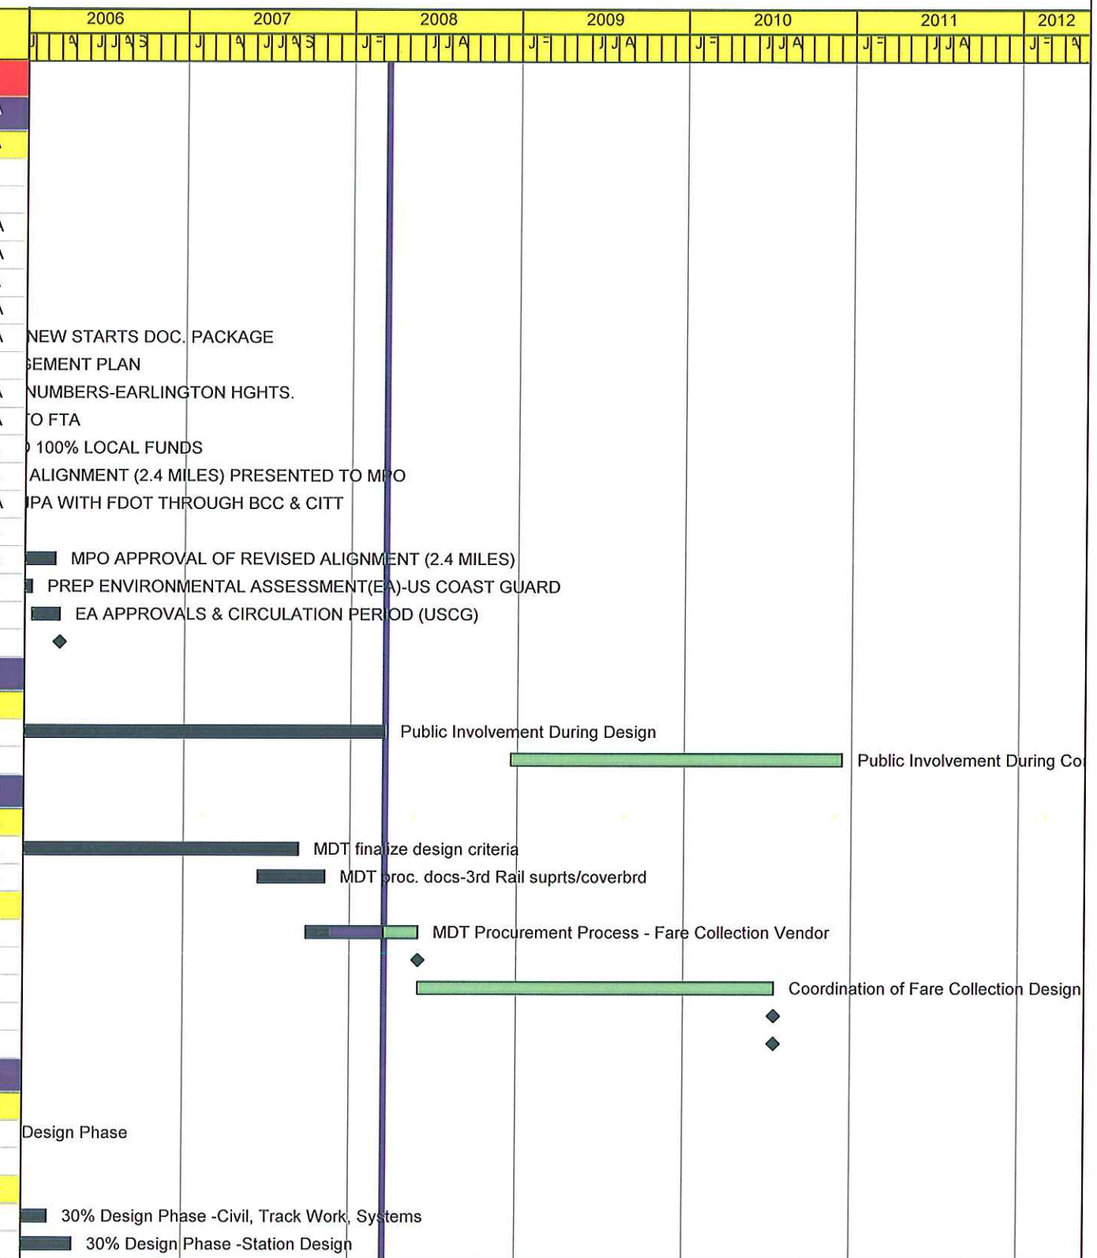

Actual Work
Remaining Work
Critical Remaining Work
Milestone
% Complete

Start Date: 01-Jun-00
Finish Date: 17-Dec-11
Data Date: 15-Mar-08
Run Date: 11-Apr-0811:39

ME25

MIAMI-DADE TRANSIT (MDT) - MAJOR CAPITAL PROJECTS

MIC-EH Connector Schedule

PROJECT MASTER SCHEDULE

MARCH 2008 SCHEDULE UPDATE

Activity ID	Activity Name	Original Duration	Remaining Duration	Total Float	Activity % Complete	Start	Finish
DE131	Submit 30% Civil., Struct, Systems Plans	4	0		100%	02-Feb-06 A	06-Feb-06 A
DE130	Submit 30% Architectural Design	0	0		100%	13-Mar-06 A	
DE101	30% DESIGN CONTROL POINT-CIVIL,TRACKWORK,SYSTEMS	0	0		100%		29-Mar-06 A
DE135	Cost Estimate to MDT For Review (30% Design)	0	0		100%	18-Apr-06 A	
DE230	VALUE ENGINEERING (DURING FINAL DESIGN)	14	0		100%	25-Apr-06 A	15-May-06 A
DE105	30% STATION DESIGN CONTROL POINT	0	0		100%		05-May-06 A
60 % DESIGN		236	0	0		07-Feb-06 A	11-Jan-07 A
DE115	60% Design Phase	274	0		100%	07-Feb-06 A	13-Oct-06 A
DE160	Wind Tunnel Test on Station Structures	108	0		100%	15-Apr-06 A	13-Jul-06 A
DE165	Submit 60% Plans and Specifications	0	0		100%		13-Oct-06 A
DE170	Cost Estimate (60% Design)	25	0		100%	13-Oct-06 A	11-Jan-07 A
DE180	MDT Comment Resolution Mtg. (60% Design)	16	0		100%	24-Oct-06 A	20-Dec-06 A
DE116	60% DESIGN CONTROL POINT	0	0		100%		11-Jan-07 A
90 % DESIGN		386	10	7		02-Oct-06 A	29-Mar-08
DE240	90% Design Thru Submittal of Plans & Spec	317	0		100%	02-Oct-06 A	31-Jul-07 A
SC100	MDT DIRECTIVE: TEMPORARY DESIGN SUSPENSION	96	0		100%	17-Nov-06 A	21-Feb-07 A
DE245	90% DESIGN CONTROL POINT	0	0		100%		31-Jul-07 A
DE265	Issue Draft Safety & Security Design Criteria	0	0		100%		06-Sep-07 A
DE190	Submit 90% Cost Estimate	0	0		100%	07-Sep-07 A	
DE266	URS Submits Design Variances for ERB Approval	46	0	10	100%	07-Sep-07 A	15-Mar-08
DE200	MDT Comment Resolution Mtg. - (90% Design)	39	0		100%	25-Sep-07 A	08-Nov-07 A
DE260	ERB Approval of Design Criteria Variance	0	0	10	0%		29-Mar-08
100 % DESIGN		99	0	6		01-Oct-07 A	17-Mar-08
DE250	100% Design Phase	69	0		100%	01-Oct-07 A	31-Dec-07 A
DE210	Submit 100% Plans and Spec.	0	0		100%	31-Dec-07 A	
DE255	100% DESIGN CONTROL POINT 1	0	0		100%		31-Dec-07 A
DE220	Final Correction & Issue Signed & Sealed Dwgs.	22	0		100%	02-Jan-08 A	31-Jan-08 A
DE275	100% DESIGN CONTROL POINT 2	0	0	8	0%		17-Mar-08
DE280	Submit 100% Cost Estimate	0	0	8	0%		17-Mar-08
GEOTECHNICAL ENGINEERING		575	0	980		06-Jan-06 A	31-Jan-08 A
GE010	Geotech Eng.- Borings & Report at Sites w/Access	645	0		100%	06-Jan-06 A	31-Jan-08 A
GE020	Issues Geotechnical Report	0	0		100%		31-Jan-08 A
RIGHT OF WAY ACQUISITIONS		911	303	677		01-Nov-05 A	13-May-09
ROW - General		853	245	332		01-Nov-05 A	21-Feb-09
ROW020	Right-of-Way Engineering - Phase 1	154	0		100%	01-Nov-05 A	24-May-06 A
ROW025	JUA WITH MDX FOR RIGHT-OF-WAY ACQUISITION	622	21	97	96.62%	01-Feb-06 A	04-Apr-08
ROW040	Preliminary Appraisals	145	0		100%	07-Apr-06 A	19-Oct-06 A
ROW030	Right-of-Way Engineering - Phase 2	363	15	69	95.87%	24-May-06 A	04-Apr-08
ROW045	MDX/MDT Joint Parcel Sketches	441	15	97	96.6%	01-Aug-06 A	04-Apr-08
ROW1004	MDX Review & Board Approval	61	61	97	0%	05-Apr-08	04-Jun-08
ROW1009	County Approval	27	27	97	0%	05-Jun-08	01-Jul-08
ROW999	Final Certification of Right-of-Way	0	0	465	0%		21-Feb-09
ROW - DEMOLITION		548	227	274		09-Apr-07 A	13-May-09
ROW1024	JPA w/MDX for 134 Demo (NCP004-TR06-CT1) (DP#1)	0	0		100%	09-Apr-07 A	
ROW1014	MDX Parcels Demolition - Parcel 134 - (DP#1)	180	0		100%	11-Apr-07 A	28-Sep-07 A
ROW1029	Demolition Contract No. NCP004-TR06-CT2 (DP#2)	0	0		100%	03-Oct-07 A	
ROW1034	Demolition Contract No. 3 (DP#3)	0	0	63	0%	01-Jul-08	
ROW1044	Demolition Contract No. 4 (DP#4)	0	0	184	0%	15-Aug-08	
ROW1019	MDX Parcels Demo (139/144) - (By Contractor)	147	147	125	0%	18-Dec-08	13-May-09

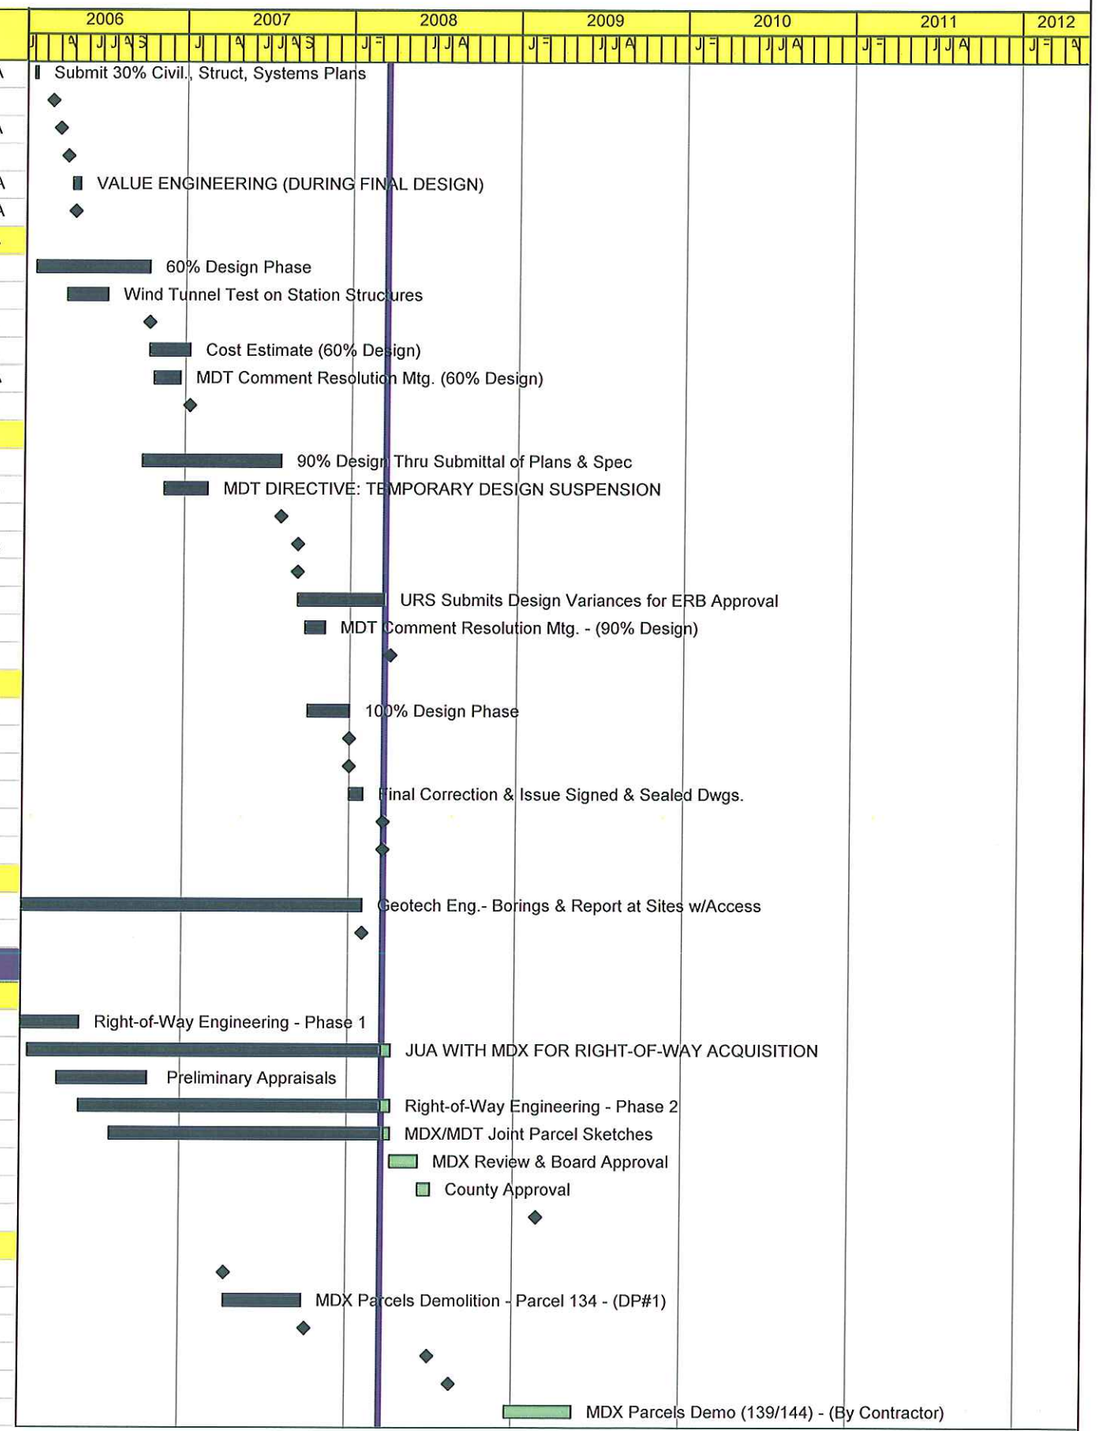

Activity ID	Activity Name	Original Duration	Remaining Duration	Total Float	Activity % Complete	Start	Finish
Parcel R-1		447	0	364		05-May-06 A	30-Jan-08 A
ROW054	Parcel R-1 Lovett Acquisition Process	84	0		100%	05-May-06 A	31-Oct-06 A
ROW056	Parcel R-1 Lovett Vacated	60	0		100%	01-Nov-06 A	02-Dec-06 A
ROW058	Parcel R-1 Lovett PM / Demolition (DP#2)	120	0		100%	03-Oct-07 A	30-Jan-08 A
Parcel R-2		455	0	466		05-May-06 A	30-Jan-08 A
ROW064	Parcel R-2 Gregory Acquisition Process	111	0		100%	05-May-06 A	01-Dec-06 A
ROW066	Parcel R-2 Gregory Vacated	30	0		100%	02-Jan-07 A	09-Jan-07 A
ROW068	Parcel R-2 Gregory PM / Demolition (DP#2)	120	0		100%	03-Oct-07 A	30-Jan-08 A
Parcel R-3		472	0	357		12-Apr-06 A	30-Jan-08 A
ROW074	Parcel R-3 Paradise Acquisition Process	123	0		100%	12-Apr-06 A	16-Feb-07 A
ROW076	Parcel R-3 Paradise Vacated	1	0		100%	16-Feb-07 A	16-Feb-07 A
ROW078	Parcel R-3 Paradise PM / Demolition (DP#2)	120	0		100%	03-Oct-07 A	30-Jan-08 A
Parcel R-4		286	0	340		12-Apr-06 A	25-May-07 A
ROW084	Parcel R-4 Kiawah Acquisition Process	409	0		100%	12-Apr-06 A	25-May-07 A
ROW086	Parcel R-4 Kiawah Vacted	1	0		100%	25-May-07 A	25-May-07 A
Parcel R-5		299	0	344		12-Apr-06 A	13-Jun-07 A
ROW094	Parcel R-5 JEG Acquisition Process	423	0		100%	12-Apr-06 A	13-Jun-07 A
ROW096	Parcel R-5 JEG Vacated	1	0		100%	13-Jun-07 A	13-Jun-07 A
Parcel R-6		460	0	318		28-Apr-06 A	30-Jan-08 A
ROW104	Parcel R-6 Hurtado Acquisition Process	123	0		100%	28-Apr-06 A	31-Jul-06 A
ROW106	Parcel R-6 Hurtado Vacated	42	0		100%	01-Aug-06 A	30-Oct-06 A
ROW108	Parcel R-6 Hurtado PM / Demolition (DP#2)	120	0		100%	03-Oct-07 A	30-Jan-08 A
Parcel R-7		490	0	318		04-May-06 A	30-Jan-08 A
ROW114	Parcel R-7 Barzola Acquisition Process	123	0		100%	04-May-06 A	31-Jul-06 A
ROW116	Parcel R-7 - Barzola Vacated	120	0		100%	01-Aug-06 A	12-Mar-07 A
ROW118	Parcel R-7 Barzola PM / Demolition (DP#2)	120	0		100%	03-Oct-07 A	30-Jan-08 A
Parcel R-8		234	0	318		12-Apr-06 A	14-Mar-07 A
ROW124	Parcel R-8 Baymen Inn Acquisition Process	127	0		100%	12-Apr-06 A	14-Feb-07 A
ROW126	Parcel R-8 Baymen Inn Vacated	1	0		100%	14-Mar-07 A	14-Mar-07 A
Parcel 121		547	124	421		26-Jul-06 A	04-Sep-08
ROW130	Parcel 121 Airport Mini Stg Appraisal Process	23	0		100%	26-Jul-06 A	28-Sep-06 A
ROW134	Parcel 121 Airport Mini Stg Acquisition Process	442	4	589	99.1%	29-Sep-06 A	18-Mar-08
ROW136	Parcel 121 Airport Mini Storage Vacated	30	30	589	0%	19-Mar-08	17-Apr-08
ROW138	Parcel 121 Airport Mini Storage PM	140	140	589	0%	18-Apr-08	04-Sep-08
Parcel 123		412	0	398		07-Jul-06 A	30-Jan-08 A
ROW140	Parcel 123 Ramari Appraisal Process	23	0		100%	07-Jul-06 A	24-Sep-06 A
ROW144	Parcel 123 Ramari Acquisition Process	207	0		100%	25-Sep-06 A	11-Jan-07 A
ROW146	Parcel 123 Ramari Vacated	180	0		100%	12-Jan-07 A	12-Mar-07 A
ROW148	Parcel 123 Ramari PM / Demolition (DP#2)	120	0		100%	03-Oct-07 A	30-Jan-08 A
Parcel 129		672	245	321		20-Jul-06 A	21-Feb-09
ROW150	Parcel 129 Hart Appraisal Process	23	0		100%	20-Jul-06 A	26-Sep-06 A
ROW154	Parcel 129 Hart Acquisition Process	444	32	762	92.79%	27-Sep-06 A	15-Apr-08
ROW158	Parcel 129 Hart PM / Demolition by Contractor	66	66	450	0%	18-Dec-08	21-Feb-09
Parcel 132		545	117	460		19-Jul-06 A	26-Aug-08
ROW160	Parcel 132 Lizy Appraisal Process	23	0		100%	19-Jul-06 A	28-Oct-06 A
ROW164	Parcel 132 Lizy Acquisition Process	489	55	644	88.75%	29-Oct-06 A	08-May-08
ROW166	Parcel 132 Lizy Vacated	22	22	644	0%	09-May-08	30-May-08
ROW173	Parcel 132 Lizy Asbestos Survey	30	30	644	0%	31-May-08	29-Jun-08
ROW168	Parcel 132 Lizy Demolition by MDT	58	58	644	0%	30-Jun-08	26-Aug-08
Parcel 133		617	240	337		29-Sep-06 A	15-Feb-09

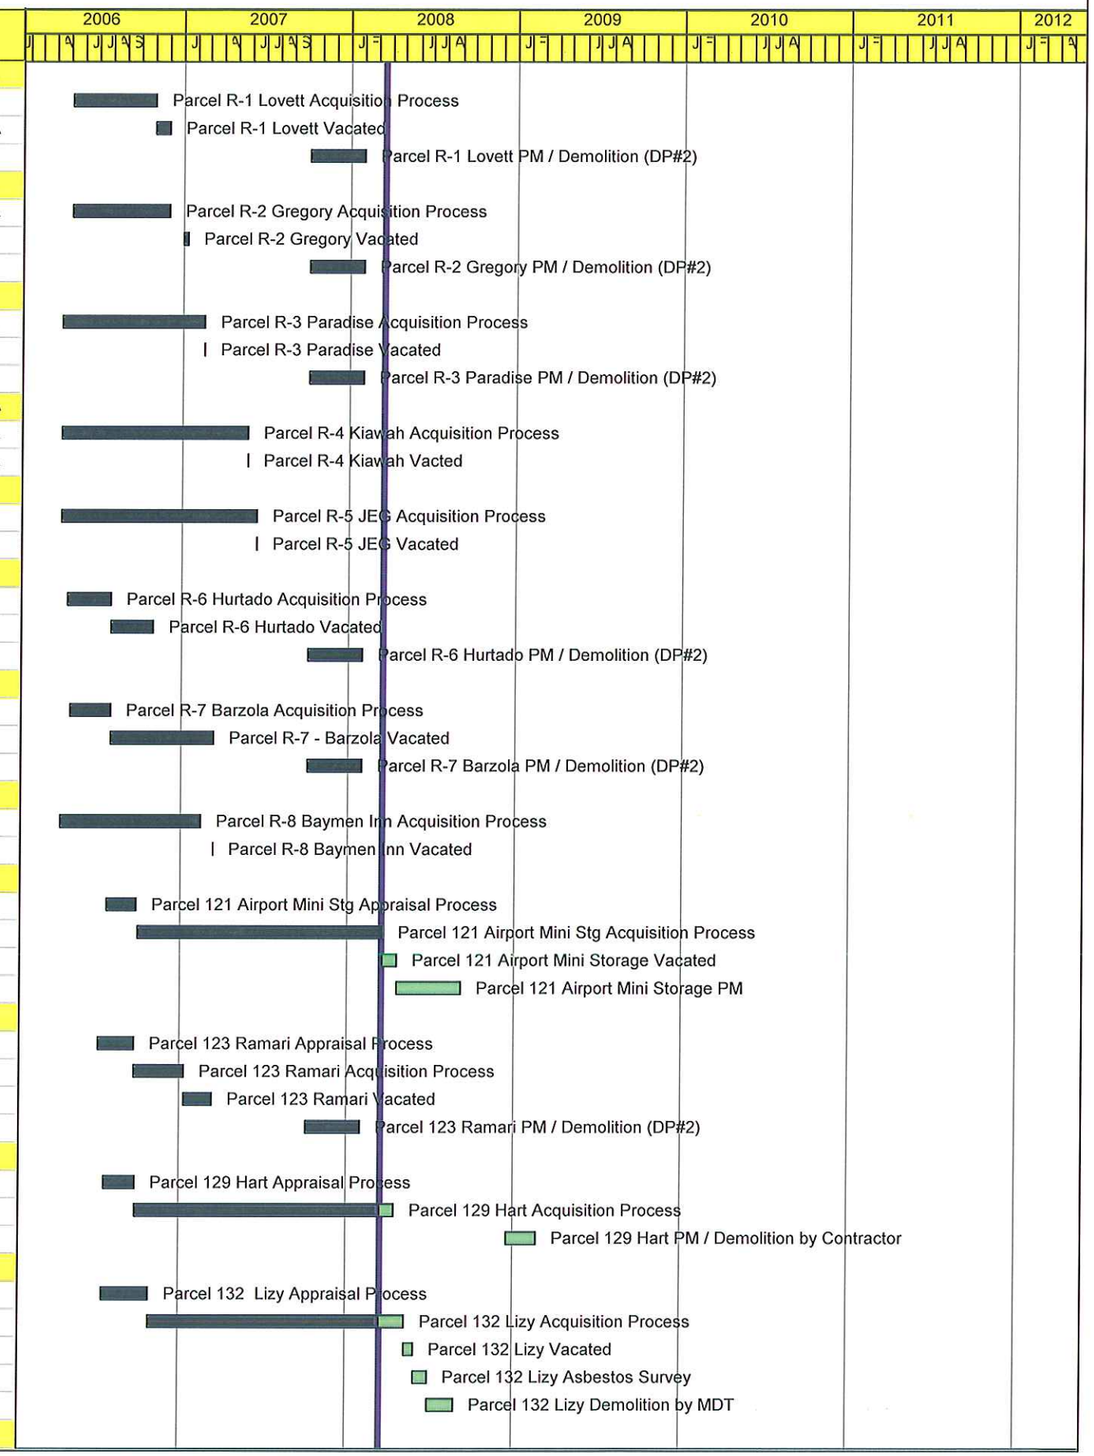

Activity ID	Activity Name	Original Duration	Remaining Duration	Total Float	Activity % Complete	Start	Finish
ROW170	Parcel 133 Johnny & Mack Appraisal Process	23	0		100%	29-Sep-06 A	23-Oct-06 A
ROW174	Parcel 133 Johnny & Mack Acquisition Process	494	0	659	100%	24-Oct-06 A	15-Mar-08
ROW176	Parcel 133 Johnny & Mack Vacated	60	60	659	0%	15-Mar-08	13-May-08
ROW181	Parcel 133 Johnny & Mack Asbestos Survey	30	30	659	0%	14-May-08	12-Jun-08
ROW178	Parcel 133 Johnny & Mack Demolition by Contractor	60	60	471	0%	18-Dec-08	15-Feb-09
Parcel 145		603	245	735		26-Oct-06 A	21-Feb-09
ROW180	Parcel 145 Eisenberg Appraisal Process	23	0		100%	26-Oct-06 A	31-Oct-06 A
ROW184	Parcel 145 Eisenberg Acquisition (Partial)	267	0		100%	01-Nov-06 A	25-Jun-07 A
ROW201	Parcel 145 Eisenberg Possible Full Acquisition	250	91	625	63.6%	25-Jun-07 A	13-Jun-08
ROW186	Parcel 145 Eisenberg Vacated	27	27	625	0%	14-Jun-08	10-Jul-08
ROW191	Parcel 145 Eisenberg Asbestos Survey	30	30	1225	0%	11-Jul-08	09-Aug-08
ROW188	Parcel 145 Eisenberg Demolition by Contractor	66	66	465	0%	18-Dec-08	21-Feb-09
Parcel 155		357	89	19		13-Oct-06 A	17-Jul-08
ROW190	Parcel 155 City Nat'l Bank Appraisal Process	23	0		100%	13-Oct-06 A	30-Oct-06 A
ROW198	Parcel 155 City Nat'l Bank Acquisition Process	487	125	27	74.33%	31-Oct-06 A	17-Jul-08
Parcel 170		392	61	269		26-Jul-06 A	09-Jun-08
ROW200	Parcel 170 Simkins Appraisal Process	23	0		100%	26-Jul-06 A	24-Oct-06 A
ROW208	Parcel 170 Simkins Acquisition Process	464	87	375	81.25%	25-Oct-06 A	09-Jun-08
Parcel 501		425	185	114		16-Apr-07 A	28-Nov-08
ROW210	Parcel 501 FPT Florida Land Appraisal Process	187	0	49	100%	16-Apr-07 A	15-Mar-08
ROW214	Parcel 501 FPT Florida Land Acquisition Process	103	103	49	0%	15-Mar-08	25-Jun-08
ROW216	Parcel 501 FPT Florida Land Vacated	60	60	160	0%	26-Jun-08	24-Aug-08
ROW218	Parcel 501 FPT Florida Land Cure by Current Owner	96	96	160	0%	25-Aug-08	28-Nov-08
Parcel 311		606	183	132		26-Jul-06 A	26-Nov-08
ROW220	Parcel 311 Gomez Appraisal Process	23	0		100%	26-Jul-06 A	01-Oct-06 A
ROW224	Parcel 311 Gomez Acquisition Process	486	0	277	100%	19-Sep-06 A	15-Mar-08
ROW226	Parcel 311 Gomez Vacated	30	30	277	0%	15-Mar-08	13-Apr-08
ROW231	Parcel 311 Gomez Asbestos Survey	30	30	277	0%	14-Apr-08	13-May-08
ROW228	Parcel 311 Gomez Demolition (DP#4)	104	104	184	0%	15-Aug-08	26-Nov-08
Parcel 312		507	77	45		01-Nov-06 A	15-Oct-08
ROW234	Parcel 312 Island Shipping Acquisition Process	207	0		100%	01-Nov-06 A	19-Jan-07 A
ROW236	Parcel 312 Island Shipping Vacated	119	0		100%	20-Jan-07 A	03-May-07 A
ROW238	Parcel 312 Island Shipping PM/Demolition (DP#3)	107	107	63	0%	01-Jul-08	15-Oct-08
Parcel 196		606	183	137		26-Jul-06 A	26-Nov-08
ROW240	Parcel 196 Hertz Appraisal Process	23	0		100%	26-Jul-06 A	24-Oct-06 A
ROW244	Parcel 196 Hertz Acquisition Process	450	47	184	89.56%	25-Oct-06 A	30-Apr-08
ROW248	Parcel 196 Hertz PM / Demolition (DP#4)	104	104	191	0%	15-Aug-08	26-Nov-08
Parcel 197		576	153	153		26-Jul-06 A	15-Oct-08
ROW250	Parcel 197 Perera Appraisal Process	23	0		100%	26-Jul-06 A	27-Sep-06 A
ROW254	Parcel 197 Perera Acquisition Process	400	0	111	100%	28-Sep-06 A	15-Mar-08
ROW256	Parcel 197 Perera Vacated	30	30	111	0%	15-Mar-08	13-Apr-08
ROW261	Parcel 197 Perera Asbestos Survey	30	30	111	0%	14-Apr-08	13-May-08
ROW258	Parcel 197 Perera Demolition (DP#3)	107	107	215	0%	01-Jul-08	15-Oct-08
Parcel 198		576	153	173		26-Jul-06 A	15-Oct-08
ROW260	Parcel 198 Fuentes Appraisal Process	23	0		100%	26-Jul-06 A	29-Sep-06 A
ROW264	Parcel 198 Fuentes Acquisition Process	398	0	63	100%	30-Sep-06 A	15-Mar-08
ROW266	Parcel 198 Fuentes Vacated	43	43	63	0%	15-Mar-08	26-Apr-08
ROW271	Parcel 198 Fuentes Asbestos Survey	48	48	63	0%	27-Apr-08	13-Jun-08
ROW268	Parcel 198 Fuentes Demolition (DP#3)	107	107	243	0%	01-Jul-08	15-Oct-08
Parcel 260 (FDOT)		676	140	58		15-Feb-06 A	26-Sep-08

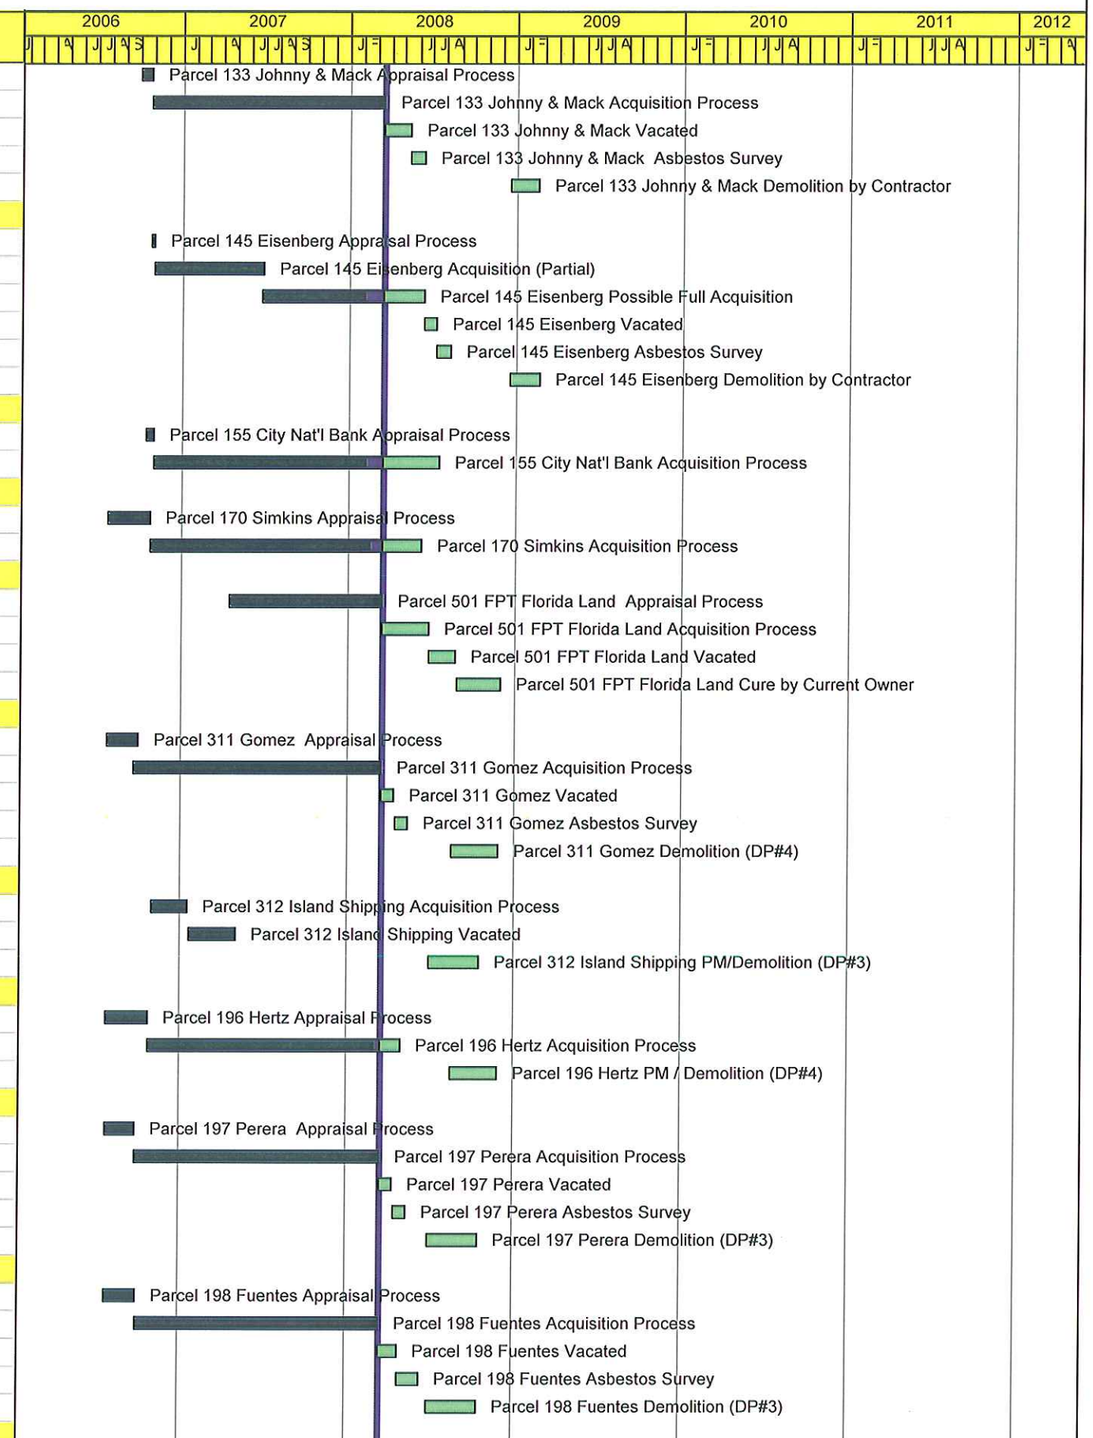

Activity ID	Activity Name	Original Duration	Remaining Duration	Total Float	Activity % Complete	Start	Finish
ROW275	Parcel 260 Rinker Negotiate Vacation of Property	457	0		100%	15-Feb-06 A	15-Mar-08 A
ROW305	Parcel 260 Rinker - Vacate to New Site	46	46	82	0%	15-Mar-08	29-Apr-08
ROW276	Parcel 260 Rinker - FDOT Remediation/Demolition	150	150	82	0%	30-Apr-08	26-Sep-08
C1-ST095	Parcel 260 Rinker: ROW Clear	0	0	82	0%		26-Sep-08
Parcel 261 (FDOT)		185	185	13		15-Mar-08	28-Nov-08
ROW290	Parcel 261 FDOT Negotiate vacation of Property	59	59	19	0%	15-Mar-08	12-May-08*
ROW292	Parcel 261 FDOT Agreement between MDT & FDOT	76	76	76	0%	15-Mar-08	29-May-08
ROW294	Parcel 261 FDOT Vacated	60	60	19	0%	13-May-08	11-Jul-08
ROW296	Parcel 261 FDOT Remediation/Demolition	140	140	19	0%	12-Jul-08	28-Nov-08
BID AND AWARD		1327	152	46		07-Aug-03 A	14-Oct-08
BID & AWARD		1327	152	46		07-Aug-03 A	14-Oct-08
BA005	PROGRAM MANAGEMENT CONSULTANT SELECTION	584	0		100%	07-Aug-03 A	01-Jun-05 A
BA010	FINAL DESIGN/SYSTEMS CONSULTANT SELECTION	327	0		100%	26-May-04 A	17-Apr-05 A
DE031	RFP CE&I DESIGN CONSULTANT SELECTION	0	0		100%	09-Oct-07 A	
DE021	MIC-EHT CE&I CONSULTANT SELECTION	300	214	64	28.67%	09-Oct-07 A	14-Oct-08
DE041	NTP TO CE&I CONSULTANT	0	0	64	0%		14-Oct-08
PTP BID & AWARD EXPEDITE		360	197	0		31-Jul-07 A	16-Dec-08
BID & AWARD		360	197	0		31-Jul-07 A	16-Dec-08
BA020	COMPLETE DESIGN (90% DESIGN)	0	0		100%		31-Jul-07 A
BA095	FIRST FTA CONCURRENCE LETTER	0	0		100%		27-Aug-07 A
BA025	PLANS,SPECS & ESTIMATE REVIEW IN-HOUSE (MDT)	29	0		100%	05-Oct-07 A	01-Nov-07 A
BA285	FTA REVIEW COMMENTS	0	0		100%		24-Oct-07 A
BA030	DBE GOAL SET BY MDT OFFICE OF CIVIL RIGHTS	29	0		100%	02-Nov-07 A	13-Dec-07 A
BA070	CONTRACT,INSUR.& BONDS APPROVED BY RISK MGMT.	29	0		100%	02-Nov-07 A	31-Jan-08 A
BA035	MDT STAFF PREPARES CONTRACT TERMS AND CONDITIONS	37	0		100%	02-Nov-07 A	07-Mar-08 A
BA040	MDT STAFF PREPARES REQUEST-TO-ADVERTISE	21	0		100%	14-Dec-07 A	03-Jan-08 A
BA045	REQUEST-TO-ADVERTISE REVIEWED BY COUNTY ATTORNEY	2	0		100%	04-Jan-08 A	04-Jan-08 A
BA310	MDT STAFF PREPARES NEWSPAPER AD	7	0		100%	04-Jan-08 A	04-Feb-08 A
BA055	REQ.-TO-ADVER. APPROVED-MDT BUDGET & MDT GRANTS	2	0		100%	07-Jan-08 A	08-Feb-08 A
BA330	NEWSPAPER AD APPROVAL- PROJECT DIRECTOR	1	0		100%	05-Feb-08 A	05-Feb-08 A
BA340	NEWSPAPER AD APPROVAL - MDT MARKETING	2	0		100%	06-Feb-08 A	07-Feb-08 A
BA065	REQUEST-TO-ADVERTISE APPROVED BY MDC BUDGET (OSMB)	24	0		100%	07-Feb-08 A	07-Feb-08 A
BA050	REQ.-TO-ADVER APPROVED-MDT DEPUTY DIR.-PLAN/DEV.	1	0		100%	08-Feb-08 A	08-Feb-08 A
BA060	REQ-TO-ADVERTISE APPROVED-MDT DIRECTOR	3	0		100%	11-Feb-08 A	11-Feb-08 A
BA295	FTA APPROVAL OF MDT CONTRACT DOCUMENTS	0	0		100%		29-Feb-08 A
BA280	STAFF PREPARES COPIES OF REQUEST-TO-ADVERTISE	2	0		100%	29-Feb-08 A	03-Mar-08 A
BA075	BID DOCUMENTS FINALIZED BY MDT STAFF	5	0		100%	03-Mar-08 A	11-Mar-08 A
BA320	REQUEST-TO-ADV. - OFFICE OF CAPITAL IMPROV APPROVAL	21	10	0	52.38%	08-Mar-08 A	24-Mar-08
BA305	FINAL PREPARATION OF THE BID DOCUMENTS	0	0		100%	12-Mar-08 A	14-Mar-08 A
BA360	REQUEST-TO-ADV. - COUNTY MANAGER APPROVAL	1	1	0	0%	24-Mar-08	24-Mar-08
BA350	REQ-TO-ADVERTISE TO MDT PLAN & DEVELOPMENT	1	1	0	0%	25-Mar-08	25-Mar-08
BA080	ADVERTISE DATE (ON THE COUNTER)	0	0	0	0%	26-Mar-08	
BA085	CONTRACTORS PREPARE BIDS	84	84	0	0%	26-Mar-08	17-Jun-08
BA090	PRE-BID CONFERENCE	0	0	55	0%	24-Apr-08	
BA100	BID OPENING	0	0	0	0%	18-Jun-08	
BA105	MDT REVIEW OF BIDS	14	14	0	0%	18-Jun-08	01-Jul-08
BA110	CONTRACTOR SUBMITS DBE INFORMATION	2	2	6	0%	20-Jun-08	21-Jun-08
BA315	FDOT REVIEW OF BIDS	14	14	0	0%	20-Jun-08	03-Jul-08
BA115	MDT DBE ADMINISTRATION REVIEW OF LOW BIDDER	7	7	6	0%	22-Jun-08	28-Jun-08

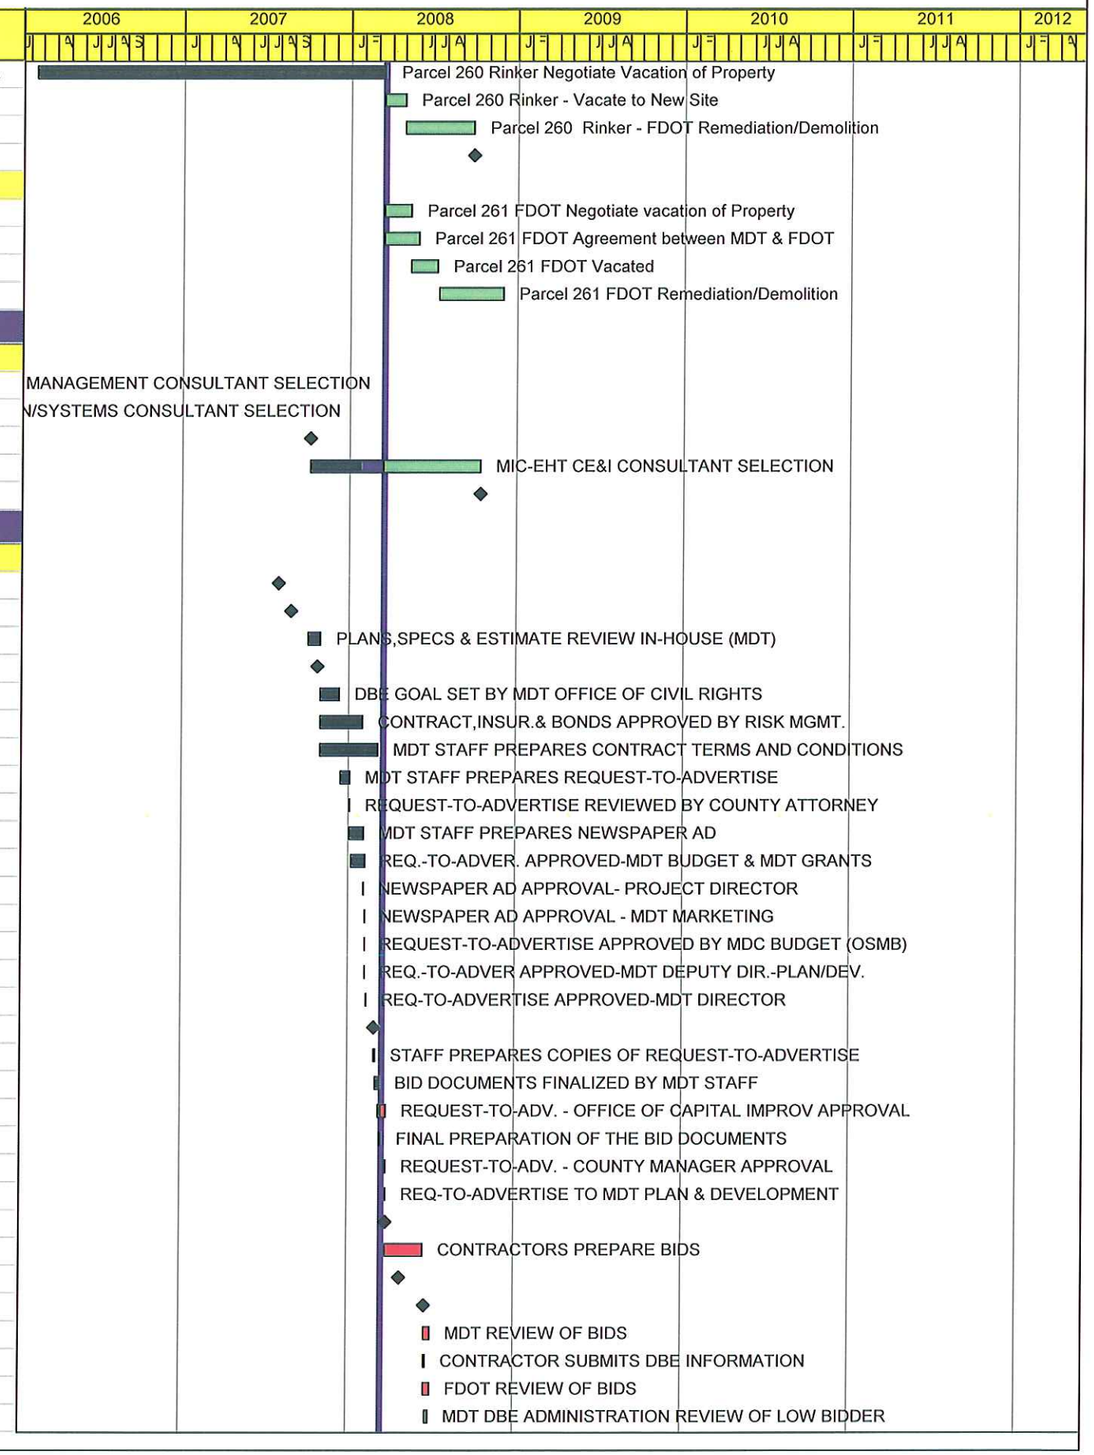

Activity ID	Activity Name	Original Duration	Remaining Duration	Total Float	Activity % Complete	Start	Finish
BA120	MDT STAFF PREPARES AWARD RECOMMENDATION	1	1	0	0%	05-Jul-08	05-Jul-08
BA325	MDT STAFF PREPARES SUPPLEMENT TO FDOT - JPA	14	14	9	0%	05-Jul-08	18-Jul-08
BA125	AWARD RECOMMENDATION REVIEWED BY CTY. ATTORNEY	4	4	0	0%	06-Jul-08	09-Jul-08
BA130	AWARD RECCOM APPROVED-MDT DEPUTY DIR.-PLAN./DEV.	1	1	0	0%	10-Jul-08	10-Jul-08
BA135	AWARD RECOMM APPROVED-MDT BUDGET & MDT GRANTS	5	5	0	0%	11-Jul-08	15-Jul-08
BA140	AWARD RECOMM. APPROVED BY MDT DIRECTOR	2	2	0	0%	16-Jul-08	17-Jul-08
BA145	AWARD RECOMMENDATION APPROVED BY MDC BUDGET	7	7	0	0%	18-Jul-08	24-Jul-08
BA150	STAFF PREPARES COPIES OF AWARD RECOMMENDATION	2	2	0	0%	25-Jul-08	26-Jul-08
BA155	PACKAGE APPROVED BY DEPUTY DIRECTOR-PLAN./DEV.	1	1	0	0%	27-Jul-08	27-Jul-08
BA160	PACKAGE TO MDT AGENDA COORDINATOR'S OFFICE	1	1	0	0%	28-Jul-08	28-Jul-08
BA170	AWARD RECOMMENDATION SIGNED BY COUNTY MANAGER	14	14	0	0%	29-Jul-08	11-Aug-08
BA175	FILE AWARD RECOMMENDATION WITH THE CLERK	1	1	0	0%	12-Aug-08	12-Aug-08
BA180	AWARD RECOMMENDATION TO MDT PLANNING & DEVELOP.	1	1	0	0%	13-Aug-08	13-Aug-08
BA185	AWARD NOTIFICATION SENT TO ALL BIDDERS	0	0	0	0%	14-Aug-08	
BA190	PROTEST PERIOD	14	14	0	0%	14-Aug-08	27-Aug-08
BA195	AWARD RECOMM. APPROVED BY CITT SUBCOMMITTEES	11	11	33	0%	01-Sep-08	11-Sep-08
BA200	AWARD RECC APPROVAL-TRANSPORTATION COMMITTEE	1	1	0	0%	10-Sep-08	10-Sep-08
BA205	BCC CYCLE-AWARD RECOMMENDATION	20	20	0	0%	11-Sep-08	30-Sep-08
BA210	BCC APPROVAL OF AWARD RECOMMENDATION	1	1	0	0%	07-Oct-08	07-Oct-08
BA220	MAYOR VETO PERIOD	10	10	12	0%	08-Oct-08	17-Oct-08
BA215	AWARD RECOMMENDATION APPROVED BY FULL CITT	15	15	0	0%	15-Oct-08	29-Oct-08
BA225	AWARD RECOMMENDATION TO MDT PLANNING & DEVELOP.	1	1	0	0%	30-Oct-08	30-Oct-08
BA230	STAFF PREPARES 5 SETS OF CONTRACTS FOR EXECUTION	5	5	0	0%	31-Oct-08	04-Nov-08
BA235	CONTRACTOR EXECUTES CONTRACT,INSURANCE & BONDS	14	14	0	0%	05-Nov-08	18-Nov-08
BA240	CONTRACT,INSUR. & BONDS REVIEWED BY CTY.ATTORNEY	3	3	0	0%	19-Nov-08	21-Nov-08
BA245	CONTRACT,INSUR.& BONDS APPROVED BY RISK MGMT.	5	5	0	0%	22-Nov-08	26-Nov-08
BA250	CONTRACT EXECUTED-CTY MGR & CLERK OF THE BOARD	7	7	0	0%	28-Nov-08	04-Dec-08
BA255	EXECUTED CONTRACT TO MDT PLANNING & DEVELOPMENT	1	1	0	0%	09-Dec-08	09-Dec-08
BA260	STAFF CONFORMS DOCUMENTS	7	7	0	0%	10-Dec-08	16-Dec-08
BA265	PRE-CONSTRUCTION CONFERENCE	0	0	0	0%		16-Dec-08
ART IN PUBLIC PLACES		649	250	632		29-Aug-06 A	02-Mar-09
ART IN PUBLIC PLACES		649	250	632		29-Aug-06 A	02-Mar-09
AP010	Call to Artist	30	0		100%	29-Aug-06 A	29-Sep-06 A
AP015	Prepare Selection Materials From Applicant Pool	45	0		100%	01-Oct-06 A	20-Nov-06 A
AP020	Schedule Prof. Advisory Committee Mtg. (PAC-1)	1	0		100%	11-Dec-06 A	11-Dec-06 A
AP025	Artist Proposal Contract Negotiation	30	0		100%	16-Dec-06 A	30-Jan-07 A
AP030	County Contract Execution	30	0		100%	01-Feb-07 A	28-Feb-07 A
AP035	Proj. Orientation Mtg. w/A&E Team, Agency, AIPP	1	0		100%	13-Mar-07 A	13-Mar-07 A
AP040	Shortlisted Artists Dev. Conceptl/Schematic Prop	40	0		100%	13-Mar-07 A	27-Apr-07 A
AP045	Schedule Prof. Advisory Committee Mtg. (PAC-2)	0	0		100%		27-Apr-07 A
AP050	Contract Negotiations w/Commissioned Artist	60	0		100%	01-Sep-07 A	31-Dec-07 A
AP055	County Contract Execution	31	46	884	0%	01-Jan-08 A	29-Apr-08
AP060	Artist Starts Design Development	90	90	884	0%	17-Jun-08	14-Sep-08
AP065	Artist Completes 60% Design Development	0	0	884	0%		16-Sep-08
AP070	Artist Completes Design Development (100%)	138	138	884	0%	30-Sep-08	14-Feb-09
AP075	APP Approves & Starts Negotiation-Phase II-F&I	0	0	884	0%	02-Mar-09	
PERMIT PROCESS		699	160	38		10-Feb-06 A	26-Oct-08
PERMITS		699	160	38		10-Feb-06 A	26-Oct-08
PP010	USCG Bridge Permit	506	0		100%	10-Feb-06 A	24-Aug-06 A

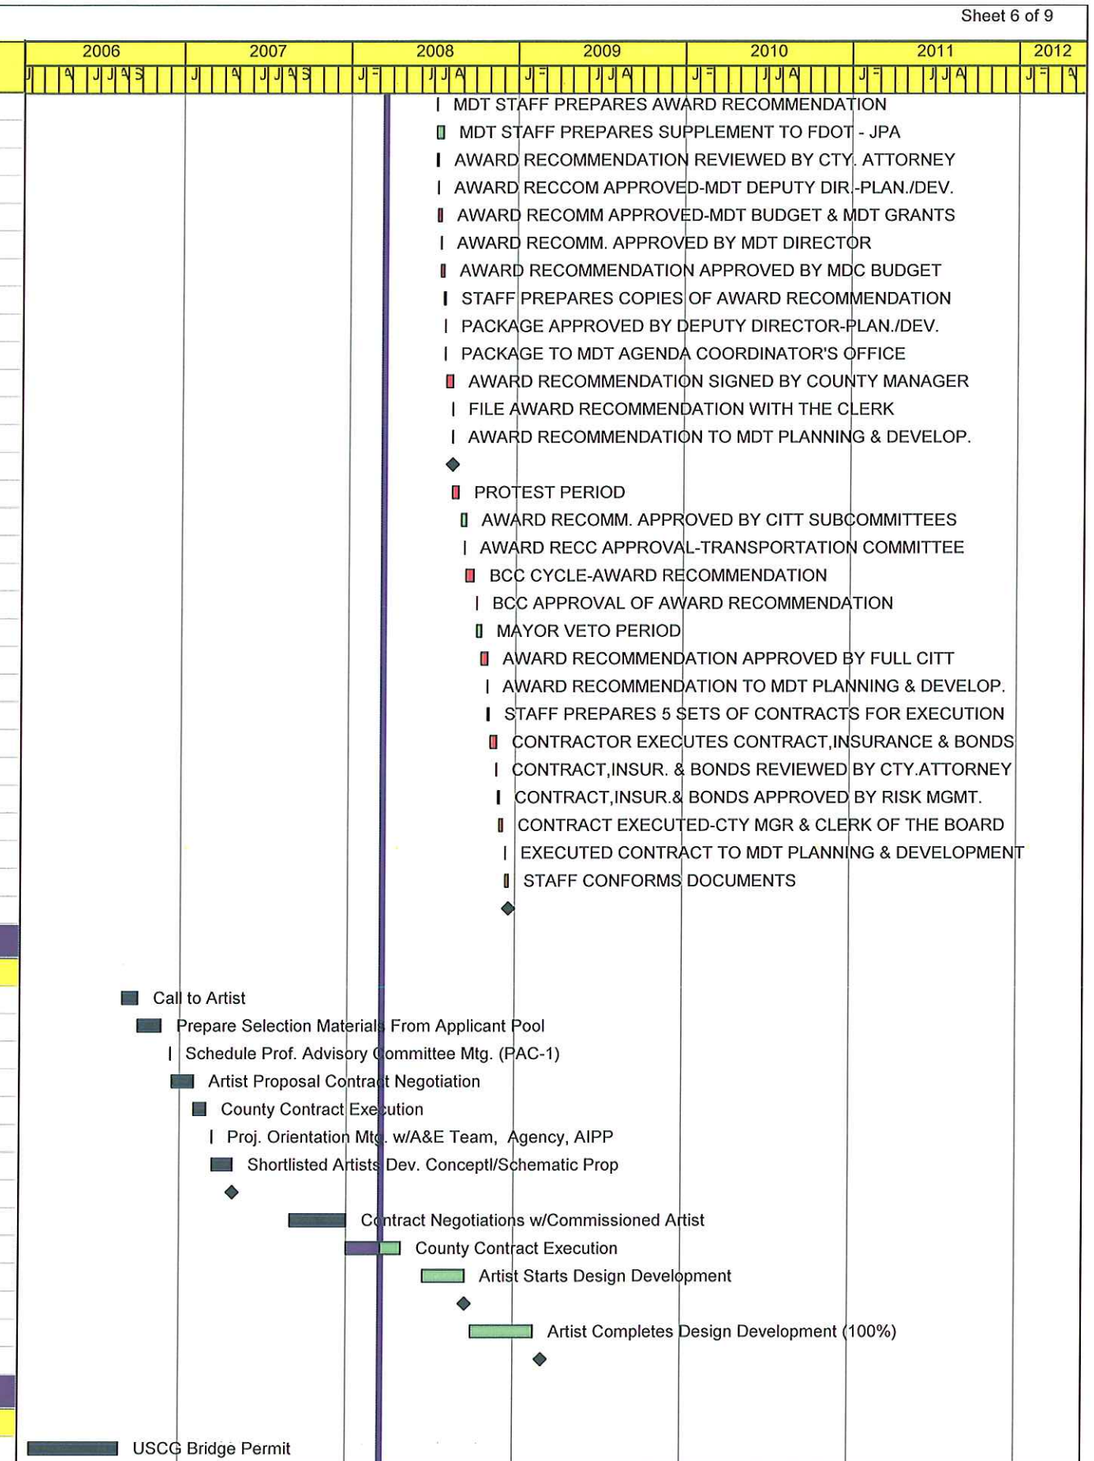

Activity ID	Activity Name	Original Duration	Remaining Duration	Total Float	Activity % Complete	Start	Finish
PP020	Issue Permit (Contingent on NEPA Aproval)	0	0		100%		24-Aug-06 A
PP100	MD DERM Class II/VI Drainage Discharge Permit	318	0	278	100%	11-Dec-06 A	15-Mar-08
PP120	MD DERM Class I Coastal Construction Permit	283	0	278	100%	11-Dec-06 A	15-Mar-08
PP030	SFWMD ERP	442	226	52	48.87%	11-Dec-06 A	26-Oct-08
PP050	SFWMD Right of Way Occupancy Permit	230	0		100%	22-Dec-06 A	27-Mar-07 A
PP080	SFWMD Water Use Permit For Dewatering	361	156	122	56.79%	22-Dec-06 A	17-Aug-08
PP060	Issue ROW Occupancy Permit	0	0		100%		27-Mar-07 A
PP070	ROW Permit Issuance (8 wk min.)	0	0		100%		27-Mar-07 A
PP140	Miami Dade County Building Permit	143	143	135	0%	15-Mar-08	04-Aug-08
PP110	Issue Drainage Discharge Permit (4 wk)	0	0	278	0%		15-Mar-08
PP130	Issue Class I Coastal Construction Permit (4 wk)	0	0	278	0%		15-Mar-08
PP150	Issue County Building Permit	0	0	135	0%		04-Aug-08
PP090	Issue Water Use Permit for Dewatering (8 wk)	0	0	122	0%		17-Aug-08
PP040	Issue ERP Permit (8 wk min)	0	0	52	0%		26-Oct-08
PP160	Obtain Permits Prior to Construction	0	0	52	0%		26-Oct-08
UTILITIES		985	589	391		01-Sep-06 A	17-Jun-10
FPL DESIGN/PERMITS/PROC. PROCESS-DISTRIBUTION		396	20	380		01-Sep-06 A	13-Apr-08
UR305	Binding Estimate - FPL Distribution Relocation	323	0		100%	01-Sep-06 A	07-Feb-07 A
UR300	FPL - Design - Distribution	395	0		100%	01-Sep-06 A	31-Jan-08 A
UR310	Define Easements - FPL Distribution Relocation	303	0		100%	01-Oct-06 A	23-Oct-07 A
UR315	MDT/FPL Negotiation & BCC Approval	32	0		100%	05-May-07 A	05-Jun-07 A
UR320	FPL Contractor Selection/Award	30	0		100%	14-Dec-07 A	25-Jan-08 A
UR350	FPL - Permitting - Distribution	30	30	532	0%	14-Dec-07 A	13-Apr-08
FPL DESIGN/PERMITTING/PROC. PROCESS-TRANSMISSION		581	185	130		01-Sep-06 A	30-Nov-08
UR005	FPL - Design and Permitting - Transmission	491	0		100%	01-Sep-06 A	31-Jan-08 A
UR008	Binding Estimate	318	0		100%	01-Oct-06 A	20-Jul-07 A
UR011	Define Easement	335	0		100%	01-Oct-06 A	23-Oct-07 A
UR014	MDT/FPL Negotiation & BCC Approval	32	0		100%	01-Oct-07 A	01-Nov-07 A
UR020	MDT/PWD Acquire Easements	260	260	181	0%	15-Mar-08	29-Nov-08
UR017	Order Utilities	61	61	88	0%	01-Oct-08	30-Nov-08
AT&T DESIGN/PERMITTING/PROCUREMENT PROCESS		409	54	107		01-Oct-06 A	29-May-08
UR330	Binding Estimate	270	0		100%	01-Oct-06 A	27-Dec-06 A
UR325	AT&T - Design and Permitting	365	46	151	87.4%	01-Oct-06 A	29-Apr-08
UR340	MDT/ AT&T Negotiation & BCC Approval	32	0		100%	03-May-07 A	05-Jun-07 A
UR345	AT&T Contractor Selection & Award	30	30	151	0%	01-Jan-08 A	29-May-08
FPL - UTILITY RELOCATION - DISTRIBUTION		307	286	694		28-Jan-08 A	20-Apr-09
UR060	FPL Obtain Permit and Issue Work Order	0	0		100%		28-Jan-08 A
UR175	FPL - Remove OHE sta 214+60	3	0		100%	28-Jan-08 A	31-Jan-08 A
UR205	FPL - Relocate OHE sta 249+90 @ Pier 87W	3	0		100%	28-Jan-08 A	31-Jan-08 A
UR210	FPL - Relocate OHE sta 259+60 @ Pier 96W to Pier 97W	25	76	510	0%	31-Jan-08 A	29-May-08
UR220	FPL - Relocate OHC sta 241+20 @ Pier	2	2	1371	0%	15-Mar-08	16-Mar-08
UR230	FPL - Relocate OHC sta 236+92 @ Pier	2	2	1371	0%	15-Mar-08	16-Mar-08
UR250	FPL - Relocate OHC sta 161+80 @ Pier	3	3	1370	0%	15-Mar-08	17-Mar-08
UR165	FPL - Relocate OHE sta 197+40 & 197+80 @ P48 to P49	7	7	902	0%	15-Mar-08	21-Mar-08
UR260	FPL - Relocate OHC sta 158+25 @ Pier	7	7	1366	0%	15-Mar-08	21-Mar-08
UR240	FPL - Relocate OHC sta 225+97 @ Pier	21	21	1352	0%	15-Mar-08	04-Apr-08
UR270	FPL - Relocate OHC sta 142+35 @ Pier	30	30	1343	0%	15-Mar-08	13-Apr-08
UR215	FPL - Relocate OHE sta 245+70 to 250+00 @ Pier 84 to 87	60	60	476	0%	15-Mar-08	13-May-08
UR195	FPL - Relocate OHE sta 230+10	3	3	757	0%	19-Apr-08	21-Apr-08

Activity ID	Activity Name	Original Duration	Remaining Duration	Total Float	Activity % Complete	Start	Finish
UR190	FPL - Relocate OHE sta 227+15	3	3	745	0%	17-May-08	19-May-08
UR125	FPL - Relocate OHE sta 176+50 @ Pier 34 to Pier 35	10	10	808	0%	18-Jul-08	27-Jul-08
UR170	FPL - Relocate OHE sta 205+00 @ Pier 53 to Pier 54	7	7	323	0%	18-Sep-08	24-Sep-08
UR145	FPL - Relocate OHE sta 183+50 @ Pier 38 to Pier 39	7	7	323	0%	25-Sep-08	01-Oct-08
UR155	FPL - Relocate OHE sta 190+40 @ Pier 43 to Pier 44	7	7	560	0%	20-Nov-08	26-Nov-08
UR115	FPL - Relocate OHE sta 165+50 @ Pier 26 to Pier 27	21	21	276	0%	05-Dec-08	25-Dec-08
UR150	FPL - Relocate OHE sta 188+50 & 189+00 @ Pier 42	14	14	583	0%	25-Dec-08	07-Jan-09
UR200	FPL - Relocate OHC sta 240+63 @ Pier 80W	3	3	232	0%	01-Jan-09	03-Jan-09
UR140	FPL - Relocate OHE & OFO sta 183+10 @ P38 to P39	7	7	298	0%	01-Jan-09	07-Jan-09
UR100	FPL - Relocate OHE sta 157+50 - 160+00	14	14	357	0%	08-Jan-09	21-Jan-09
UR130	FPL - Relocate OHE sta 179+20 @ Pier 35 to Pier 36	14	14	572	0%	20-Feb-09	05-Mar-09
UR135	FPL - Relocate OHE sta 180+80	5	5	579	0%	22-Feb-09	26-Feb-09
UR160	FPL - Relocate OHE sta 193+10 & 194+40	3	3	482	0%	24-Feb-09	26-Feb-09
UR110	FPL - Relocate OHE sta 164+80 - 172+30 @ P27 to P31	30	30	176	0%	03-Mar-09	01-Apr-09
UR180	FPL - Relocate Fibernet OHC sta 164+80 @ P27	3	3	160	0%	18-Apr-09	20-Apr-09
FPL - UTILITY TRANSMISSION		109	109	101		03-Mar-09	31-Jul-09
UR105	FPL - Reloc 138KV OHTrans sta 159+22 - 170+42 @ P24E to P31	121	121	88	0%	03-Mar-09	01-Jul-09
UR120	FPL - Relocate 230KV OHTrans sta 172+10 @ P31 to P32	30	30	143	0%	02-Jul-09	31-Jul-09
FPL - NEW SERVICE		589	589	156		15-Mar-08	17-Jun-10
UR070	FPL - New Service Design	270	270	220	0%	15-Mar-08	09-Dec-08
UR072	Binding Estimate - New Service	30	30	220	0%	10-Dec-08	08-Jan-09
UR074	MDT Approval - New Service	60	60	220	0%	09-Jan-09	09-Mar-09
UR076	New Service Construction	465	465	220	0%	10-Mar-09	17-Jun-10
C1-SS485	FPL Feeder Installation Complete	0	0	220	0%		17-Jun-10
AT&T - UTILITY RELOCATION		207	207	391		30-May-08	16-Mar-09
UR071	BEGIN UTILITY RELOCATION CONSTRUCTION	0	0	105	0%	30-May-08	
UR575	AT&T - Removal, Cut & Cap Conduit sta 143+10 @ Pier 8W	7	7	320	0%	04-Jul-08	10-Jul-08
UR550	AT&T - Relocate BC NW 41st St 213+00 - 234+20	60	60	267	0%	12-Jul-08	09-Sep-08
UR560	AT&T - Relocate Traffic Controller sta 239+64 @ Pier 79	30	30	421	0%	18-Nov-08	17-Dec-08
UR525	AT&T - Relocate OHC sta 188+50 @ Pier 41 to Pier 42	21	21	298	0%	04-Dec-08	24-Dec-08
UR545	AT&T - Remove OHC sta 244+45 to 250+00 @ Pier 83W	45	45	213	0%	04-Dec-08	17-Jan-09
UR555	AT&T - Remove BC sta 164+60 @ Pier 26	2	2	485	0%	18-Dec-08	19-Dec-08
UR520	AT&T - Relocate OHC sta 183+00 @ Pier 38	7	7	298	0%	25-Dec-08	31-Dec-08
UR500	AT&T - Relocate OHC sta 157+50 - 158+00 @ Pier 20	7	7	357	0%	01-Jan-09	07-Jan-09
UR515	AT&T - Relocate OFO & OHC sta 179+20 @ Pier 35 to Pier 36	45	45	572	0%	06-Jan-09	19-Feb-09
UR535	AT&T - Remove OHC sta 194+40 @ Pier 46	2	2	450	0%	22-Feb-09	23-Feb-09
UR530	AT&T - Relocate OHC sta 190+40 @ Pier 43	21	21	450	0%	24-Feb-09	16-Mar-09
WASD - UTILITY RELOCATION		39	39	263		18-Nov-08	09-Jan-09
UR935	WASD - Cut & Cap 6" Water Main 255+90 @ Pier 92W	7	7	233	0%	18-Nov-08	24-Nov-08
UR945	WASD - Relocate FH & 12" Water Main 171+95 @ Pier 31	7	7	376	0%	04-Dec-08	10-Dec-08
UR955	WASD - Relocate 6" Water Main 158+00 @ Pier 20	7	7	369	0%	03-Jan-09	09-Jan-09
MDPWD - UTILITY RELOCATION		121	121	63		18-Dec-08	04-Jun-09
UR930	MDPWD - Relocate Traffic Controller Sta 240+00 @ Pier 79	14	14	232	0%	18-Dec-08	31-Dec-08
UR960	MDPWD - Relocate BC Sta 240+00 @ Pier 79	14	14	235	0%	18-Dec-08	31-Dec-08
UR940	MDPWD - Relocate Traffic Controller 239+90 @ Pier 87W	14	14	151	0%	07-Mar-09	20-Mar-09
UR950	Relocate Storm Sewer 207+80 - 254+00	90	90	89	0%	07-Mar-09	04-Jun-09
FCG - UTILITY RELOCATION		301	301	294		04-Jun-08	29-Jul-09
UR820	FCG - Cap & Abandon Gas Line Sta 212+85 to 216+60 @ Pier 58 - 61	7	7	747	0%	04-Jun-08	10-Jun-08
UR810	FCG - Relocate 6" Gas Line Sta 158+00 @ Pier 20	15	15	466	0%	04-Jun-08	18-Jun-08
UR805	FCG - Relocate 1 1/4 Gas 173+25 Pier 32	14	14	775	0%	18-Jul-08	31-Jul-08

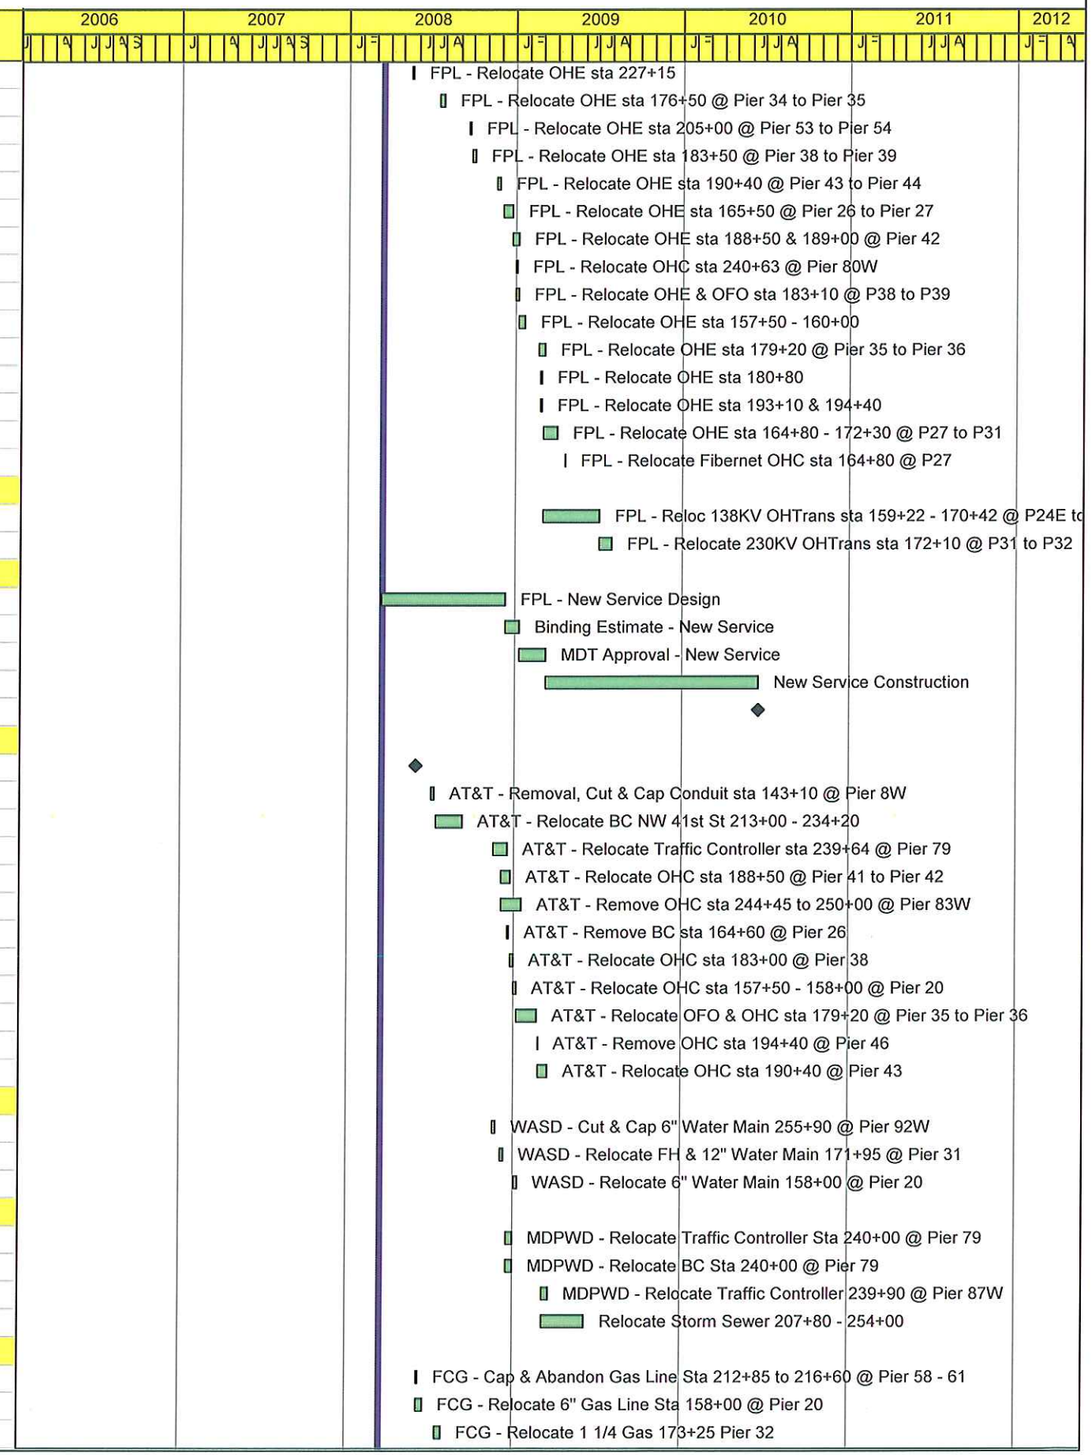
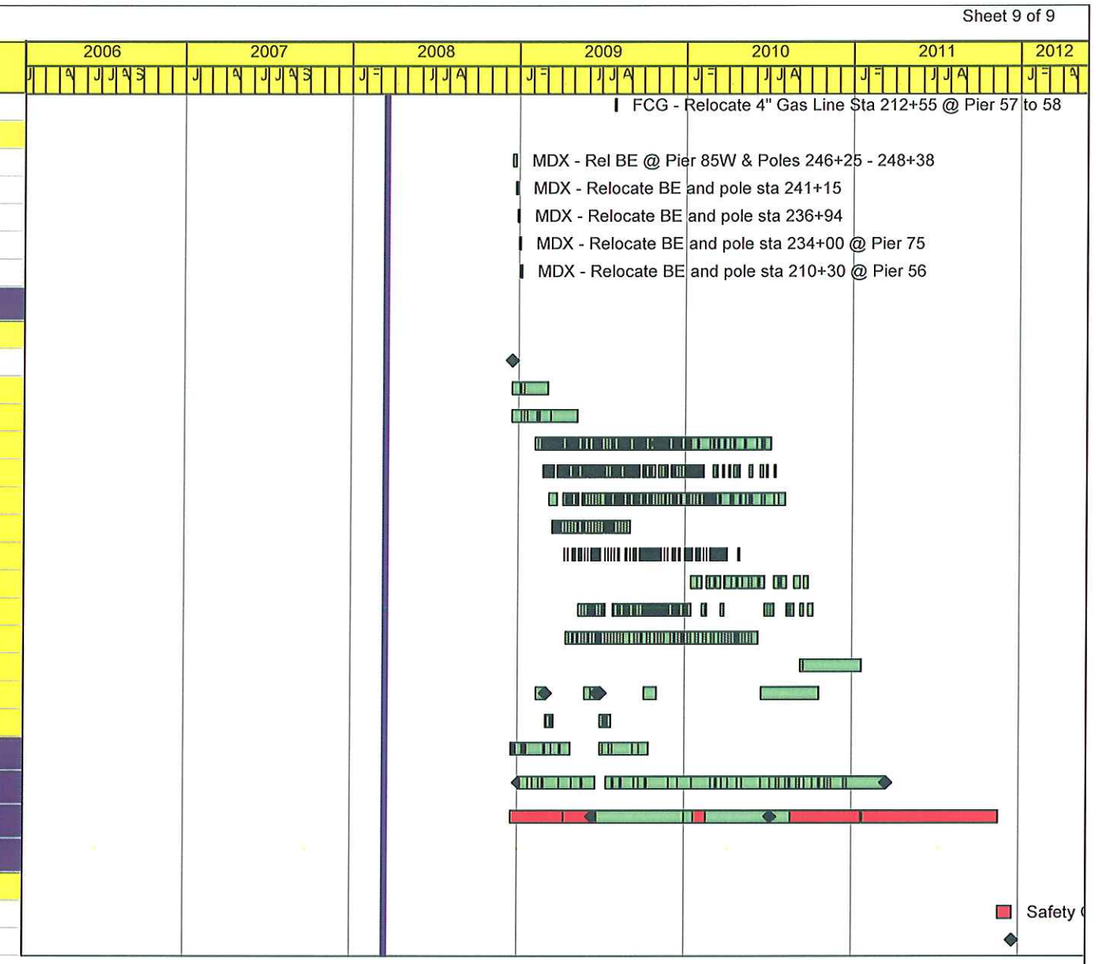
Activity ID	Activity Name	Original Duration	Remaining Duration	Total Float	Activity % Complete	Start	Finish
UR830	FCG - Relocate 4" Gas Line Sta 212+55 @ Pier 57 to 58	4	4	77	0%	26-Jul-09	29-Jul-09
MDX - UTILITY RELOCATION		13	13	300		18-Dec-08	05-Jan-09
UR920	MDX - Rel BE @ Pier 85W & Poles 246+25 - 248+38	7	7	251	0%	18-Dec-08	24-Dec-08
UR915	MDX - Relocate BE and pole sta 241+15	3	3	323	0%	25-Dec-08	27-Dec-08
UR910	MDX - Relocate BE and pole sta 236+94	3	3	402	0%	28-Dec-08	30-Dec-08
UR905	MDX - Relocate BE and pole sta 234+00 @ Pier 75	3	3	402	0%	31-Dec-08	02-Jan-09
UR900	MDX - Relocate BE and pole sta 210+30 @ Pier 56	3	3	420	0%	03-Jan-09	05-Jan-09
CONSTRUCTION - GUIDEWAY		546	546	153		17-Dec-08	20-Jan-11
NOTICE TO PROCEED		0	0	0		17-Dec-08	17-Dec-08
BA270	NOTICE-TO-PROCEED (NTP)	0	0	0	0%		17-Dec-08
MOBILIZATION		57	57	63		18-Dec-08	06-Mar-09
PROCUREMENT		102	102	65		18-Dec-08	08-May-09
FOUNDATIONS		367	367	75		07-Feb-09	06-Jul-10
COLUMNS		365	365	89		23-Feb-09	16-Jul-10
CAPITALS		370	370	81		09-Mar-09	06-Aug-10
UBEAM FABRICATION		122	122	272		16-Mar-09	01-Sep-09
UBEAM ERECTION		272	272	113		13-Apr-09	27-Apr-10
CANTILEVEL BALANCED SEGMENTALS		182	182	56		14-Jan-10	25-Sep-10
SPAN TO SPAN SEGMENTAL		367	367	56		13-May-09	07-Oct-10
DECK		301	301	92		14-Apr-09	08-Jun-10
SOUND WALLS		97	97	153		08-Sep-10	20-Jan-11
TRACK WORK		441	441	58		10-Feb-09	19-Oct-10
STRUCTURE - DEMOLITION		103	103	124		03-Mar-09	23-Jul-09
CONSTRUCTION - SUBSTATIONS		214	214	202		18-Dec-08	13-Oct-09
CONSTRUCTION - MIC STATION		574	574	98		03-Jan-09	17-Mar-11
SYSTEMS PROCUREMENT & INSTALLATION		759	759	23		18-Dec-08	15-Nov-11
PUNCH LIST, CERTIFICATION & REVENUE READY		23	23	0		16-Nov-11	17-Dec-11
REVENUE READY		23	23	0		16-Nov-11	17-Dec-11
C1-SS490	Safety Certifications	32	32	0	0%	16-Nov-11	17-Dec-11
C1-SS500	PROJECT COMPLETE	0	0	0	0%		17-Dec-11
